




# Agenda

- **Permitting**
- **FEMA Coordination**
- **Funding**
- **Next Steps**



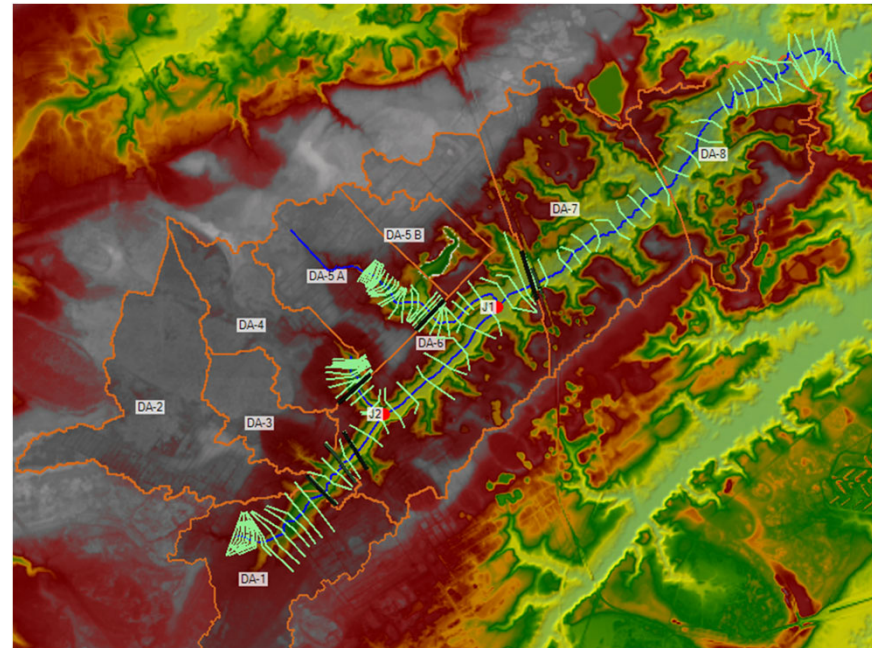

# Permitting

## Dam Safety Review


- January 14, 2021 submittal
- Received Comment mid October
- Responded on December 11, 2021
- Anticipate 30 – 60 day review

## Floodplain

- CLOMR Submittal January 14, 2021
- Responded to comments July 15, 2021, requested Fee waiver (\$8,000+)
- Technical Review and Public Notice complete
- FEMA audit underway, Anticipated Floodplain permit by mid February 2022

## Environmental Permitting

- Need MOTSU easement to get E&SC, 401/404 permits in hand

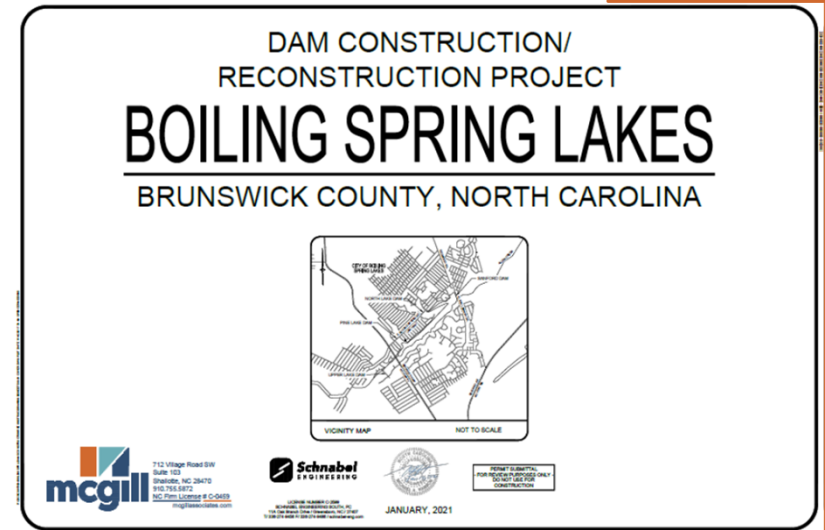



## Recent FEMA Coordination

### Sanford Dam and Upper Lake Dam #68141

- HMP approved May 3, 2021
- In EHP for final approvals

### Pine Lake Dam and North Lake Dam #126563

- HMP approved July 1, 2021
- In EHP for final approvals

### Both Projects Combined

- EHP determined EA is required
- EHP developing EA in coordination with McGill and City
- Anticipated EA completion 7/1/2022





# Funding

## Anticipated Funding Sources

- FEMA \$17.6M
- NC Legislature \$12M
- Local Share \$12M  
(USDA Rural Dev. Loan)

## Potential Additional Funding Sources

- NCORR Forgiveness \$2M
- Golden Leaf Flood Prog. TBD
- State ARPA via DWI TBD
- Federal Infra. IJA TBD





## Near Term Next Steps

- Obtain MOTSU easement and complete E&SC permitting
- NCDPS Permit to Construct (Dam Safety)
- USDA Application Part 1
- Revisit Construction Cost Estimates
- FEMA Admin Approval
- USDA Application Part 2
- Board approval of FEMA funding obligation
- NC Legislature (procedural approval)
- Bidding
- Authorize McGill Construction Management Services Task Order

