USDA-NRCS EWP Engineering Services

City of Boiling Springs Lakes

LDSI, INC

Sept 2020 - Update

TASK DESCRIPTION		PLAN START	PLAN END	
Streambank Stabilization Projects		1/27/2020	7/31/2021	551
Kickoff	Planned	1/27/2020	1/28/2020	1
	Actual	1/28/2020	1/28/2020	1
Survey & Existing Conditions	Planned	1/28/2020	3/24/2020	56
	Actual	2/3/2020	3/27/2020	53
Design Development	Planned	4/6/2020	6/30/2020	85
	Actual	4/6/2020	7/29/2020	
Permitting and Construction Documents	Planned	6/30/2020	1/1/2021	185
	Actual	7/29/2020		
Construction	Planned	2/1/2021	7/31/2021	180
	Actual			
Shoreline Stabilization Projects		1/27/2020	6/1/2021	491
Kickoff	Planned	1/27/2020	1/28/2020	1
	Actual	1/28/2020	1/28/2020	
Survey & Existing Conditions	Planned	1/28/2020	2/17/2020	20
	Actual	2/3/2020	3/27/2020	53
Design Development	Planned	2/17/2020	6/30/2020	134
	Actual	3/27/2020	7/29/2020	
Permitting and Construction Documents	Planned	6/30/2020	1/1/2021	185
	Actual	7/29/2020		
Construction	Planned	2/1/2021	6/1/2021	120
	Actual			
Dam & Levee Project		1/27/2020	12/31/2021	704
Kickoff	Planned	1/27/2020	1/28/2020	1
	Actual	1/28/2020	1/28/2020	
Survey & Existing Conditions	Planned	1/28/2020	2/17/2020	20
	Actual	2/3/2020	3/27/2020	53
Design Development	Planned	2/25/2020	7/24/2020	150
	Actual	3/27/2020	9/1/2020	
Permitting and Construction Documents	Planned	7/1/2020	1/1/2021	184
	Actual	9/1/2020		
Construction	Planned	2/1/2021	12/31/2021	333
	Actual			

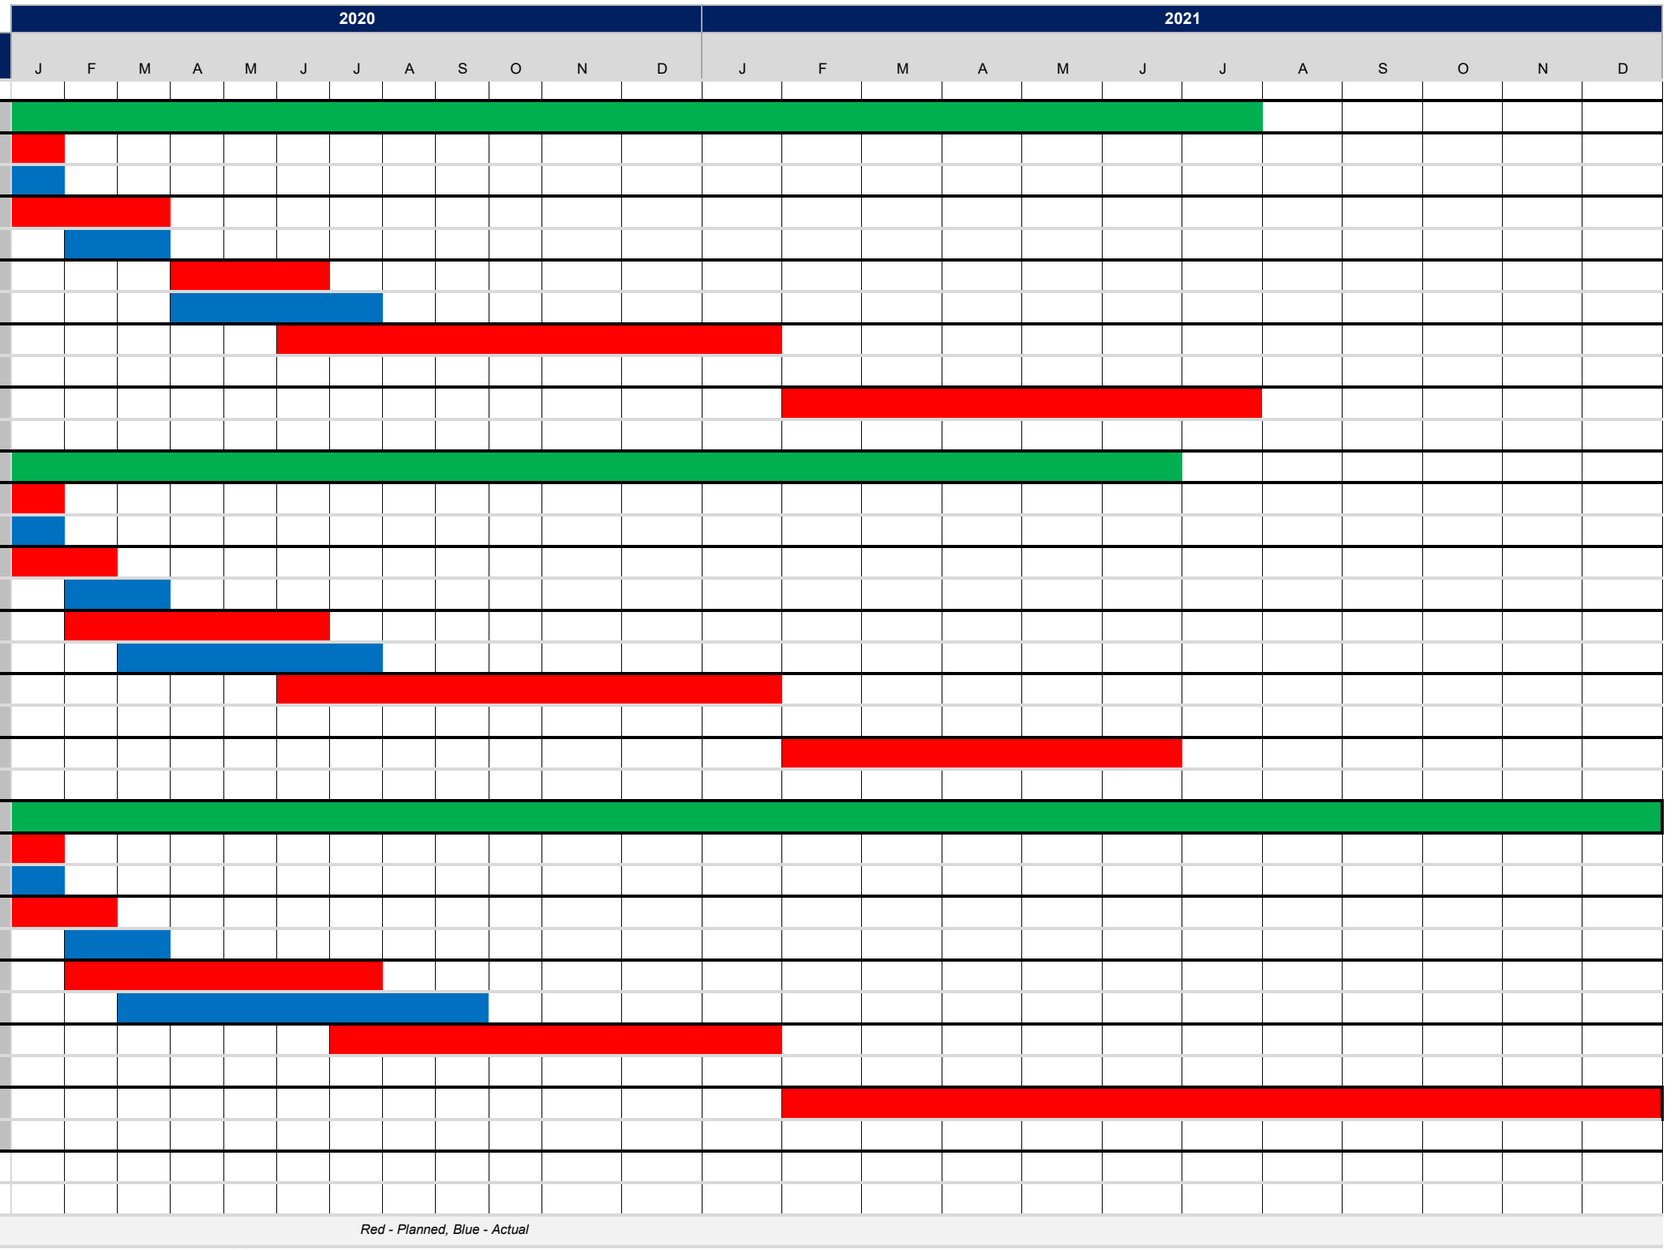

Red - Planned, Blue - Actual

The above schedule is based upon quoted and/or experienced review times and are subject to change based upon actual review times. LDSI will expedite submittals and revisions to the extent possible to help maintain the above schedules.
